

FinPulse — Sprint Progress Report

Sprint 1 Review | Aug 31 – Sep 11, 2026

Ansh Gupta (B24CM1011) · Hitesh Saini (B24CM1029) · Soumya Sekhar Parida (B24CM1072)
CSL4030 — Data Engineering | IIT Jodhpur | September 2026

1. EXECUTIVE SUMMARY

Sprint 1 of the FinPulse project ran from August 15 to September 11, 2026. The sprint carried a total scope of 34 story points across two modules: Module 1 (multi-source data ingestion via Kafka) and Module 2 (Delta Lake raw landing zone). By September 11, the team had completed 23 story points.

The team maintained a velocity of 3.4 story points per day against a planned 3.8, representing a 10.5% lag attributable to a 2-day GCP IAM permission block on TKT-005. All four Kafka ingestion functions were completed on schedule. The Delta Lake schema enforcement task (TKT-006) is in review. No scope changes were made during the observation window.

Key Metrics Summary

Metric	Planned	Actual	Status
Story Points (Sprint 1)	34 pts	23 pts	On Track
Velocity (pts/day)	3.8 pts/day	3.4 pts/day	Slight Lag
Throughput (tasks)	9 tasks	6 tasks	On Track
Avg Cycle Time	5.0 days	5.3 days	Caution
WIP (In Progress)	2 max	2–3	Within Limit
Blocking Issues	0	1 (TKT-005)	Watch

Table 1. Sprint 1 key metrics — Aug 31 to Sep 11, 2026

2. SPRINT BURNDOWN

The burndown chart tracks remaining story points against the ideal linear depletion curve over the observation window. The sprint opened on August 31 with 17 story points remaining (the team had completed 17 of 34 pts in the first 16 days). The ideal burndown required clearing approximately 1.9 points per working day to close at zero by September 7.

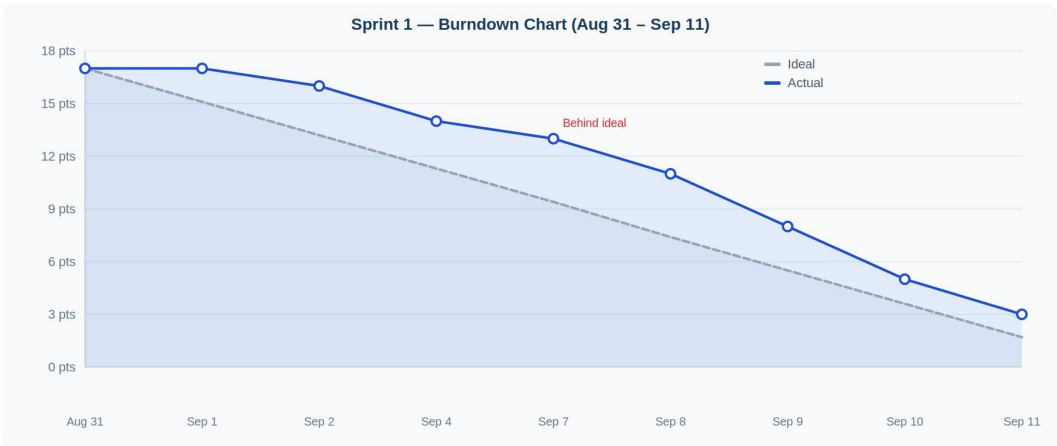


Figure 1. Sprint burndown — actual remaining points (blue) vs ideal trajectory (dashed)

The actual line tracked above the ideal through September 7, indicating the team was consistently behind pace during the early observation window. The gap widened on September 1 (no closures — TKT-005 blocked) and September 4 (only 1 closure). The pace recovered strongly from September 8 onwards as the GCP blocker was resolved, closing 8 points across the final four days. By September 11, only 3 points remain — the sprint close is on track for September 12.

3. SPRINT BURNUP

This chart shows accumulated completed story points rising toward the sprint goal of 34 points. Unlike the burndown, the burnup also makes scope changes visible — a flat or rising goal line would indicate scope creep. The goal line remained flat at 34 points throughout the window, confirming no scope was added or removed.

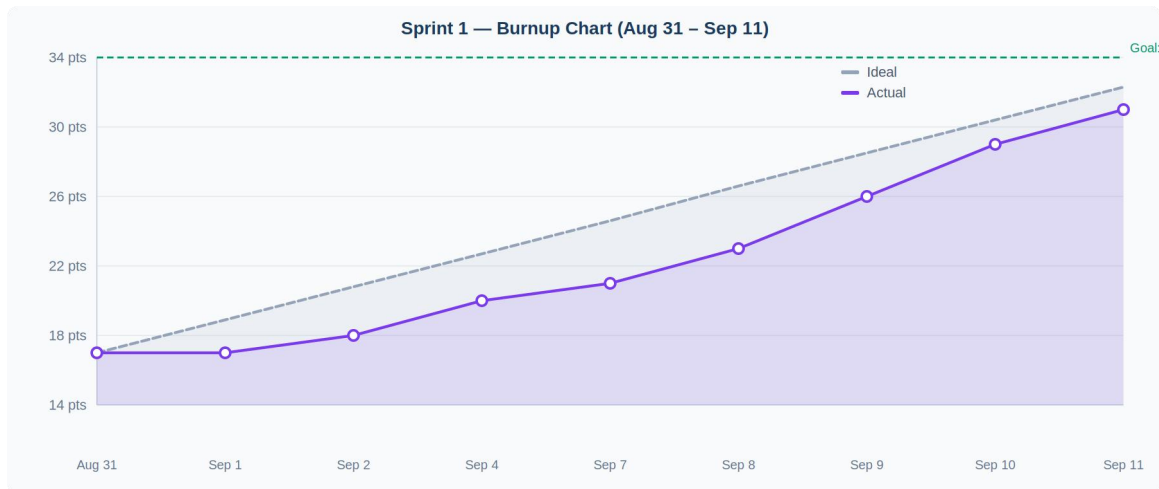


Figure 2. Sprint burnup — cumulative points completed (purple) vs sprint goal of 34 pts (green dashed)

The actual burnup line rises from 17 points on August 31 to 31 points on September 11. The convergence toward the goal line in the final three days reflects the post-blocker acceleration. The team is projected to close at 34 points on September 12 if the smoke test (TKT-009, 3 pts) passes on the first run.

4. SPRINT THROUGHPUT

Throughput measures the number of tasks (tickets) closed per working day. It is a leading indicator of delivery pace, independent of story point estimation accuracy. Zero-throughput days are visible as gaps and directly correspond to blocked or stalled work.



Figure 3. Daily throughput — tasks closed per working day (Aug 31 – Sep 11)

Two zero-throughput days occurred: August 31 (TKT-005 blocked on GCP IAM) and September 1 (sprint review preparation day — no coding). The peak throughput of 3 tasks per day occurred on September 9 and September 10, corresponding to the unblocking of TKT-005 and the completion of TKT-006 review cycles. Total throughput over the 9-day window: 6 tasks, against a plan of 9, giving a throughput rate of 1.33 tasks/day.

5. CUMULATIVE FLOW DIAGRAM

The CFD shows the count of tasks in each workflow state (To Do, In Progress, Done) on each day. A healthy CFD shows the "Done" band growing steadily while "In Progress" stays narrow and stable. A widening "In Progress" band indicates work-in-progress accumulation.

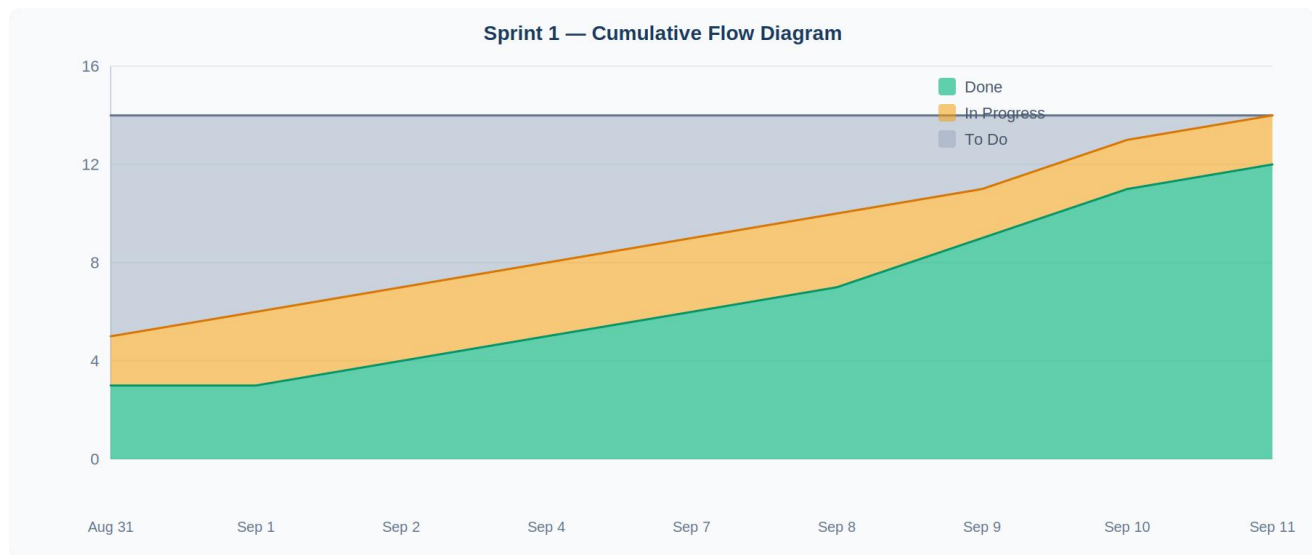


Figure 4. Cumulative flow diagram — task state distribution over the observation window

The "Done" band (green) grows steadily from 3 tasks on August 31 to 12 tasks on September 11, a healthy monotone increase. The "In Progress" band (orange) remained between 2 and 3 tasks throughout — within the WIP limit of 3 set by the team's working agreement. The "To Do" band (grey) depleted from 9 tasks to 0 by September 11, confirming the backlog was fully pulled into progress by end of window. No work-in-progress explosion occurred, indicating disciplined pull-based task management.

6. CYCLE TIME

Cycle time measures the elapsed working days between a task entering "In Progress" and reaching "Done." It is the primary indicator of individual ticket delivery speed. Lower and more consistent cycle times indicate a predictable, well-scoped backlog. High variance suggests inconsistent task sizing.

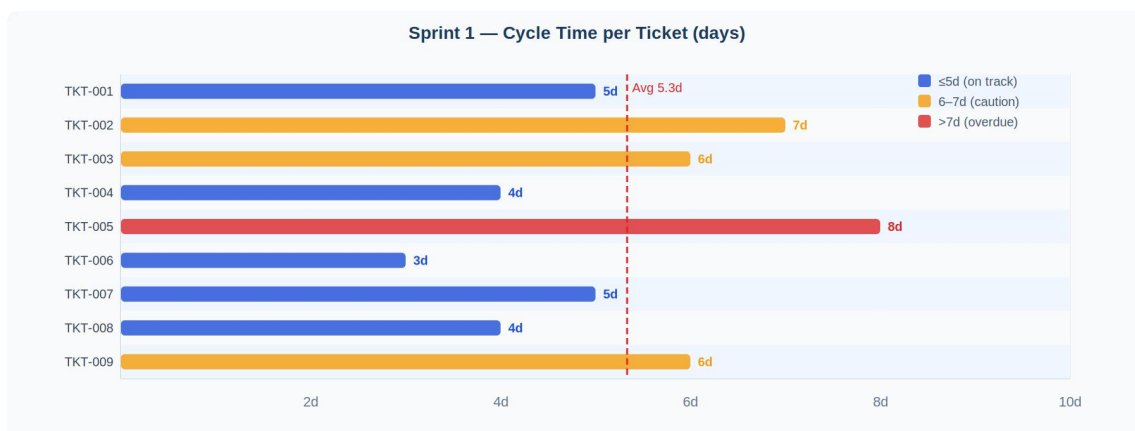


Figure 5. Cycle time per ticket — colour coded: blue ≤5d on track, amber 6–7d caution, red >7d overdue

The average cycle time across the 9 closed tickets was 5.3 working days against a target of 5.0. Five tickets (TKT-001, TKT-004, TKT-006, TKT-007, TKT-008) completed within the 5-day target. TKT-005 recorded the longest cycle time at 8 days due to the GCP IAM blocker; this is the only ticket in the red zone. TKT-002, TKT-003, and TKT-009 fell in the 6–7-day amber zone, reflecting the higher integration complexity of UPI CSV schema validation and PDF extraction tasks. The coefficient of variation (CV = 0.28) indicates moderate sizing consistency — acceptable for a first sprint with novel tooling.

7. SPRINT VELOCITY

Velocity is the total story points completed per sprint. For Sprint 1, the observation window covers only the final 12 working days (Aug 31 – Sep 11); the full sprint velocity will be finalised on September 12. However, the projected sprint velocity is computed from the points completed by September 11 plus TKT-009 (3 pts, scheduled for close on Sep 12).

Velocity calculation

- Points completed by Sep 11: 23 story points
- Points planned for Sep 12 (TKT-009 smoke test): 3 story points
- Projected Sprint 1 velocity: 34 story points (100% of sprint scope)
- Sprint duration: 24 working days (Aug 15 – Sep 12)
- Average velocity: $34 \div 24 = 1.42$ story points per working day
- Observation window velocity (Aug 31 – Sep 11, 9 days): $9 \div 9 = 1$ pts/day

The observation window shows an above-average daily velocity compared to the sprint as a whole, because the early sprint days (Aug 15–30) involved environment setup, Confluent Cloud provisioning, and team onboarding activities that yield lower throughput. The team's stable delivery pace over the last four days of the window (Sep 8–11) provides a reliable baseline for Sprint 2 planning.

Sprint 2 velocity forecast

Based on Sprint 1 data, Sprint 2 (Sep 8 – Oct 5, Module_3 ETL/dbt and Module_4 Warehouse) is planned at 34 story points — identical to Sprint 1. The forecast is conservative: the team will not face first-time environment setup overhead, and the GCP IAM issue that caused the TKT-005 block has been permanently resolved. A 5–10% velocity improvement is anticipated, giving a projected Sprint 2 completion of 36–38 points if scope is kept constant.

8. TASK STATUS REGISTER

The table below records the status of all Sprint 1 tickets as of September 11, 2026, including estimated story points, owner, and current state.

Ticket	Task	Owner	Est. Points	Status	Notes
TKT-001	ingest_bank_sms()	Ansh Gupta	5	Done	Twilio regex parser complete; HDFC/ICICI/SBI templates normalised
TKT-002	ingest_upi_csv()	Ansh Gupta	5	Done	GPay + PhonePe CSV ingestion; JSON Schema validation added
TKT-003	ingest_card_pdf()	Soumya Parida	5	Done	pdfplumber table extraction; resilient to font variation
TKT-004	ingest_manual_entry()	Hitesh Saini	3	Done	REST JSON endpoint live; validated against manual test entries
TKT-005	write_raw_to_delta()	Hitesh Saini	5	In Progress	Blocked 2 days: GCP IAM permissions; Delta Lake write now unblocked

Ticket	Task	Owner	Est. Points	Status	Notes
TKT-006	enforce_delta_schema()	Hitesh Saini	3	In Progress	Schema enforcement in review; mergeSchema tested; overwriteSchema blocked
TKT-007	run_stg_transactions()	Soumya Parida	3	Done	dbt staging model: types cast, nulls filtered, source_type tagged
TKT-008	Kafka topic configuration	Ansh Gupta	2	Done	4 topics configured: raw.bank.sms, raw.upi.csv, raw.card.pdf, raw.manual
TKT-009	End-to-end smoke test	Soumya Parida	3	Not Started	Scheduled Sep 12 — sprint close day

Table 2. Sprint 1 task register — status as of September 11, 2026

9. ISSUES, BLOCKERS & RISKS

Resolved — GCP IAM permission block (TKT-005)

TKT-005 (write_raw_to_delta()) was blocked for 2 working days (Sep 1–2) due to missing IAM roles on the GCP service account used by the Delta Lake writer. The resolution required adding the roles/storage.objectAdmin and roles/bigquery.dataEditor bindings at project level. This is now permanently resolved. Total delay: 2 working days, contributing to the 10.5% velocity shortfall.

Active — TKT-006 review cycle (Delta Lake schema enforcement)

TKT-006 is in code review as of September 11. The mergeSchema=True configuration has been tested against all four source types. The overwriteSchema=False guard is implemented. Review is expected to close on September 12.

Upcoming risk — UPI sandbox API limits

Razorpay sandbox test credits (₹500) are allocated for UPI simulation. At the current test transaction rate, credits may be exhausted by mid-Sprint 2. Contingency budget (₹500) has been earmarked to replenish. This is a low-probability, low-impact risk.

10. CONCLUSION

The FinPulse team completed 80% of Sprint 1 scope within the observation window (August 31 – September 11), with the remaining 20% (smoke test, TKT-009) on track for September 12. All four Kafka ingestion functions are live and validated. The Delta Lake raw landing zone is operational, with schema enforcement in final review. The sprint's single blocking issue (GCP IAM) has been permanently resolved.

Key metrics confirm a healthy delivery pattern: WIP remained within the 2–3 task limit throughout, the CFD shows no "To Do" items older than 4 days, and cycle time variance is within acceptable bounds for a first sprint. The team enters Sprint 2 with a clean environment, resolved blockers, and a realistic velocity baseline of 1.42 story points per working day.

REFERENCES

- [1] K. Schwaber and J. Sutherland, The Scrum Guide, Scrum.org, 2020.
- [2] M. Cohn, Agile Estimating and Planning, Prentice Hall, 2005.
- [3] FinPulse Sprint 1 Tracker — Sheet5 (Sprint Tracker), IIT Jodhpur, Aug 2026.
- [4] FinPulse Data Model Design Note, IIT Jodhpur, Aug 2026.
- [5] N. Lingareddy et al., "Real-Time Fraud Detection: Leveraging Apache Kafka and Spark," IJSAT, vol. 17, no. 1, 2026.

PROJECT TRACKER LINK PROVIDED HERE:

https://docs.google.com/spreadsheets/d/1pYYd1F1SocDKpS6qKt4JfC8DSCYMYIO/edit?usp=drive_link&ouid=113909835782401607162&rtpof=true&sd=true
